ID		Task Mode	Task Name	Duration	Start	Finish	Predecessors	Successors
1			**East Washington St. Redevelopment Project - Shelbyville**	**176 days**	**Tue 3/26/19**	**Tue 11/26/19**		
2	✓		Preconstruction Conference	1 day	Tue 3/26/19	Tue 3/26/19		
3			**Phase 1A - SR 9 to Pike St. - North Side**	**117 days**	**Thu 4/18/19**	**Mon 8/12/19**		
4	✓		**Phase 1A1 - SR 9 to Pike St. - North Side - Sanitary Sewer**	**28 days**	**Thu 4/18/19**	**Mon 5/27/19**		
5	✓		Install MOT	1 day	Thu 4/18/19	Thu 4/18/19		7FS+1 day,4
6	✓		Layout Structures	1 day	Fri 4/19/19	Fri 4/19/19	5	10
7	✓		Sawcut Pavement, Curb, Sidewalks, Islands, Center Curbs	1 day	Mon 4/22/19	Mon 4/22/19	5FS+1 day	10,8
8	✓		Install Sanitary Sewer Pipe, Structures, Laterals & Cleanout - SR 9 to Pike	24 days	Tue 4/23/19	Fri 5/24/19	5,7	9,10,22,24
9	✓		Test Sanitary	1 day	Mon 5/27/19	Mon 5/27/19	8	10
10	✓		Phase 1A1 Complete	0 days	Mon 5/27/19	Mon 5/27/19	5,6,7,8,9	25,79,86,63
11			**Phase 1A2 - SR 9 to Pike St. - North Side - Hardscape**	**82 days**	**Fri 4/19/19**	**Mon 8/12/19**	**5**	
12	✓		Layout Structures, Curb & Gutter, etc.	1 day	Fri 4/19/19	Fri 4/19/19	5	28,13,25
13	✓		Sawcut Pavement, Curb, Sidewalks, Islands, Center Curbs	2 days	Mon 4/22/19	Tue 4/23/19	12	14,28,25
14	✓		Remove Median Island at SR 9	1 day	Wed 4/24/19	Wed 4/24/19	13	15,28,25
15	✓		Remove 2 Center Curbs at Pike St.	1 day	Thu 4/25/19	Thu 4/25/19	14	28,16,25
16	✓		Remove Pavement, Curb, Sidewalks, Street Signs	4 days	Fri 4/26/19	Wed 5/1/19	15	28,32FS+10
17	✓		FPW Grade Beam	2 days	Thu 5/2/19	Fri 5/3/19	16	18,28,25,21
18	✓		Install Storm Water Pipe & Structures	16 days	Mon 5/6/19	Mon 5/27/19	17	28,23FS+50
19	✓		Install Light Pole Foundations	1 day	Fri 5/17/19	Fri 5/17/19	17FS+9 days	20,22,24,25
20	✓		Install Conduit	4 days	Mon 5/20/19	Thu 5/23/19	19	28,22,24,25
21			FPW Curb & Gutter, Curb Ramps	41 days	Wed 5/8/19	Wed 7/3/19	17FS+2 days	28,25,53,55
22			Structural Soil Mix	28 days	Mon 5/27/19	Wed 7/3/19	20,8,19	28,25
23			Install Threshold Wall	1 day	Tue 8/6/19	Tue 8/6/19	18FS+50 days	28
24			FPW Sidewalks	33 days	Mon 5/27/19	Wed 7/10/19	20,8,19	28,26,25,53
25			Patch Pavement	1 day	Thu 7/11/19	Thu 7/11/19	10,12,13,14,15,16,17	26
26			FPW Colored Stamped Concrete - North Alley	6 days	Fri 7/12/19	Fri 7/19/19	24,25	28
27			Install Planter Curb	5 days	Tue 8/6/19	Mon 8/12/19	18FS+50 days	28,48
28			Phase 1A2 Complete	0 days	Mon 8/12/19	Mon 8/12/19	12,13,14,15,16,18,20	79,86,63
29			**Phase 1B - Pike St. to Railroad - North Side**	**137 days**	**Mon 5/27/19**	**Thu 10/10/19**	**18**	
30			**Phase 1B1 - Pike St. to RR - North Side - Sanitary Sewer**	**35 days**	**Mon 5/27/19**	**Fri 7/12/19**	**18**	
31	✓		Layout Structures	1 day	Mon 5/27/19	Mon 5/27/19	18	35,32
32	✓		Remove Pavement, Curb, Sidewalks	7 days	Tue 5/28/19	Wed 6/5/19	31,16FS+10 days	35,33
33			Install Sanitary Sewer Pipe, Structures, Laterals & Cleanouts	25 days	Thu 6/6/19	Wed 7/10/19	32,18,52	34,35
34			Test Sanitary	2 days	Thu 7/11/19	Fri 7/12/19	33	35,37,36
35			Phase 1B1 Complete	0 days	Fri 7/12/19	Fri 7/12/19	31,32,33,34	79,63
36			**Phase 1B2 - Pike St. to RR - North Side - Hardscape**	**64 days**	**Mon 7/15/19**	**Thu 10/10/19**	**34**	
37			Install Storm Sewer Pipe & Structures	5 days	Mon 7/15/19	Fri 7/19/19	34	48,38
38			FPW Grade Beam	1 day	Mon 7/22/19	Mon 7/22/19	37	39,48
39			Install Light Pole Foundations	1 day	Tue 7/23/19	Tue 7/23/19	38	40,48
40			Install Conduit	4 days	Wed 7/24/19	Mon 7/29/19	39	48,41
41			FPW Curb & Gutter, Curb Ramps	10 days	Tue 7/30/19	Mon 8/12/19	40	48,42
42			FPW Concrete Drives	10 days	Tue 8/13/19	Mon 8/26/19	41	43,48,47,61
43			Structural Soil Mix	3 days	Tue 8/27/19	Thu 8/29/19	42	44,48
44			FPW Sidewalks	20 days	Fri 8/30/19	Thu 9/26/19	43	45,48
45			FPW Curb Ramps	5 days	Fri 9/27/19	Thu 10/3/19	44	48,46
46			Install Planter Curb & Threshold Wall	5 days	Fri 10/4/19	Thu 10/10/19	45	48
47			Patch Pavement	1 day	Tue 8/27/19	Tue 8/27/19	57,42	48
48			Phase 1B2 Complete	0 days	Thu 10/10/19	Thu 10/10/19	37,39,40,41,42,43,44	79,64,63
49			**Phase 2 - SR 9 to Pike St. - South Side**	**92 days**	**Tue 5/28/19**	**Tue 8/27/19**	**18**	
50	✓		Sawcut Pavement, Curb, Sidewalks	1 day	Tue 5/28/19	Tue 5/28/19	18	62,51
51	✓		Remove Pavement, Curb, Sidewalks	1 day	Wed 5/29/19	Wed 5/29/19	50	62,52
52	✓		Install Storm Water Pipe & Structures	5 days	Thu 5/30/19	Wed 6/5/19	51	33,53,62
53			Install Light Pole Foundations	1 day	Thu 7/11/19	Thu 7/11/19	52,21,24	54,62,55
54			Install Conduit	4 days	Fri 7/12/19	Wed 7/17/19	53	62,57
55			Slip Form Curb & Gutter	4 days	Fri 7/12/19	Wed 7/17/19	53,21,24	62,56,57
56			FPW Curb & Gutter, Curb Ramps	15 days	Thu 7/18/19	Wed 8/7/19	55	62
57			FPW Sidewalks	20 days	Thu 7/18/19	Wed 8/14/19	54,55	58,60,59,62
58			Install Planter Curb	5 days	Thu 8/15/19	Wed 8/21/19	57	62
59			Install Signs	1 day	Thu 8/15/19	Thu 8/15/19	57	62
60			Install Benches, Bike Loops, Waste Cans	1 day	Thu 8/15/19	Thu 8/15/19	57	62
61			Patch Pavement	1 day	Tue 8/27/19	Tue 8/27/19	57,42	62
62			Phase 2 Complete	0 days	Tue 8/27/19	Tue 8/27/19	50,51,53,54,55,57,58	79,86
63			**Phase 3 - Pike St. to Railroad - South Side**	**41 days**	**Fri 10/11/19**	**Wed 11/20/19**	**10,28,35,48**	
64			Tree Removal	1 day	Fri 10/11/19	Fri 10/11/19	48	77,65
65			Sawcut Pavement, Curb, Sidewalks	1 day	Mon 10/14/19	Mon 10/14/19	64	77,66
66			Remove Pavement, Curb, Sidewalks, Street Signs	3 days	Tue 10/15/19	Thu 10/17/19	65	67,77
67			Install Storm Water Pipe & Structures	5 days	Fri 10/18/19	Thu 10/24/19	66	68,77
68			Install Light Pole Foundations	1 day	Fri 10/25/19	Fri 10/25/19	67	70,69,77
69			Install Conduit	4 days	Mon 10/28/19	Thu 10/31/19	68	77
70			FPW Curb & Gutter, Curb Ramps	3 days	Mon 10/28/19	Wed 10/30/19	68	77,71,72
71			FPW Concrete Drives	10 days	Thu 10/31/19	Wed 11/13/19	70	77
72			FPW Sidewalks	10 days	Thu 10/31/19	Wed 11/13/19	70	73,75,74,77
73			Install Planter Curb	5 days	Thu 11/14/19	Wed 11/20/19	72	77
74			Install Signs	3 days	Thu 11/14/19	Mon 11/18/19	72	77
75			Install Benches, Bike Loops, Waste Cans	2 days	Thu 11/14/19	Fri 11/15/19	72	77
76			Patch Pavement	1 day	Thu 11/14/19	Thu 11/14/19	72	77
77			Phase 3 Complete	0 days	Wed 11/20/19	Wed 11/20/19	64,65,66,67,68,69,70	79,78
78			**Phase 4 - Resurfacing & Pavement Markings - SR 9 to RR**	**6 days**	**Thu 11/21/19**	**Tue 11/26/19**	**77**	
79			Mill & Resurface Roadway	2 days	Thu 11/21/19	Fri 11/22/19	10,28,35,48,62,77	80,81
80			Install Pavement Markings	2 days	Mon 11/25/19	Tue 11/26/19	79	81
81			Phase 3B Complete	0 days	Tue 11/26/19	Tue 11/26/19	79,80	83
82			**ICD 3 - All Hardscape from Pike St. to Railroad**	**0 days**	**Fri 12/6/19**	**Fri 12/6/19**		
83			Actual Completion	0 days	Tue 11/26/19	Tue 11/26/19	81	
84			**ICD 2 - All Landscape from SR 9 to Pike St.**	**0 days**	**Tue 10/15/19**	**Tue 10/15/19**		
85			**ICD 1 - All Hardscape from SR 9 to Pike St.**	**0 days**	**Sat 8/31/19**	**Sat 8/31/19**		
86			Actual Completion	0 days	Tue 8/27/19	Tue 8/27/19	10,28,62	
87			**Contract Completion - All Landscape from Pike St. to Railroad**	**0 days**	**Fri 5/22/20**	**Fri 5/22/20**		

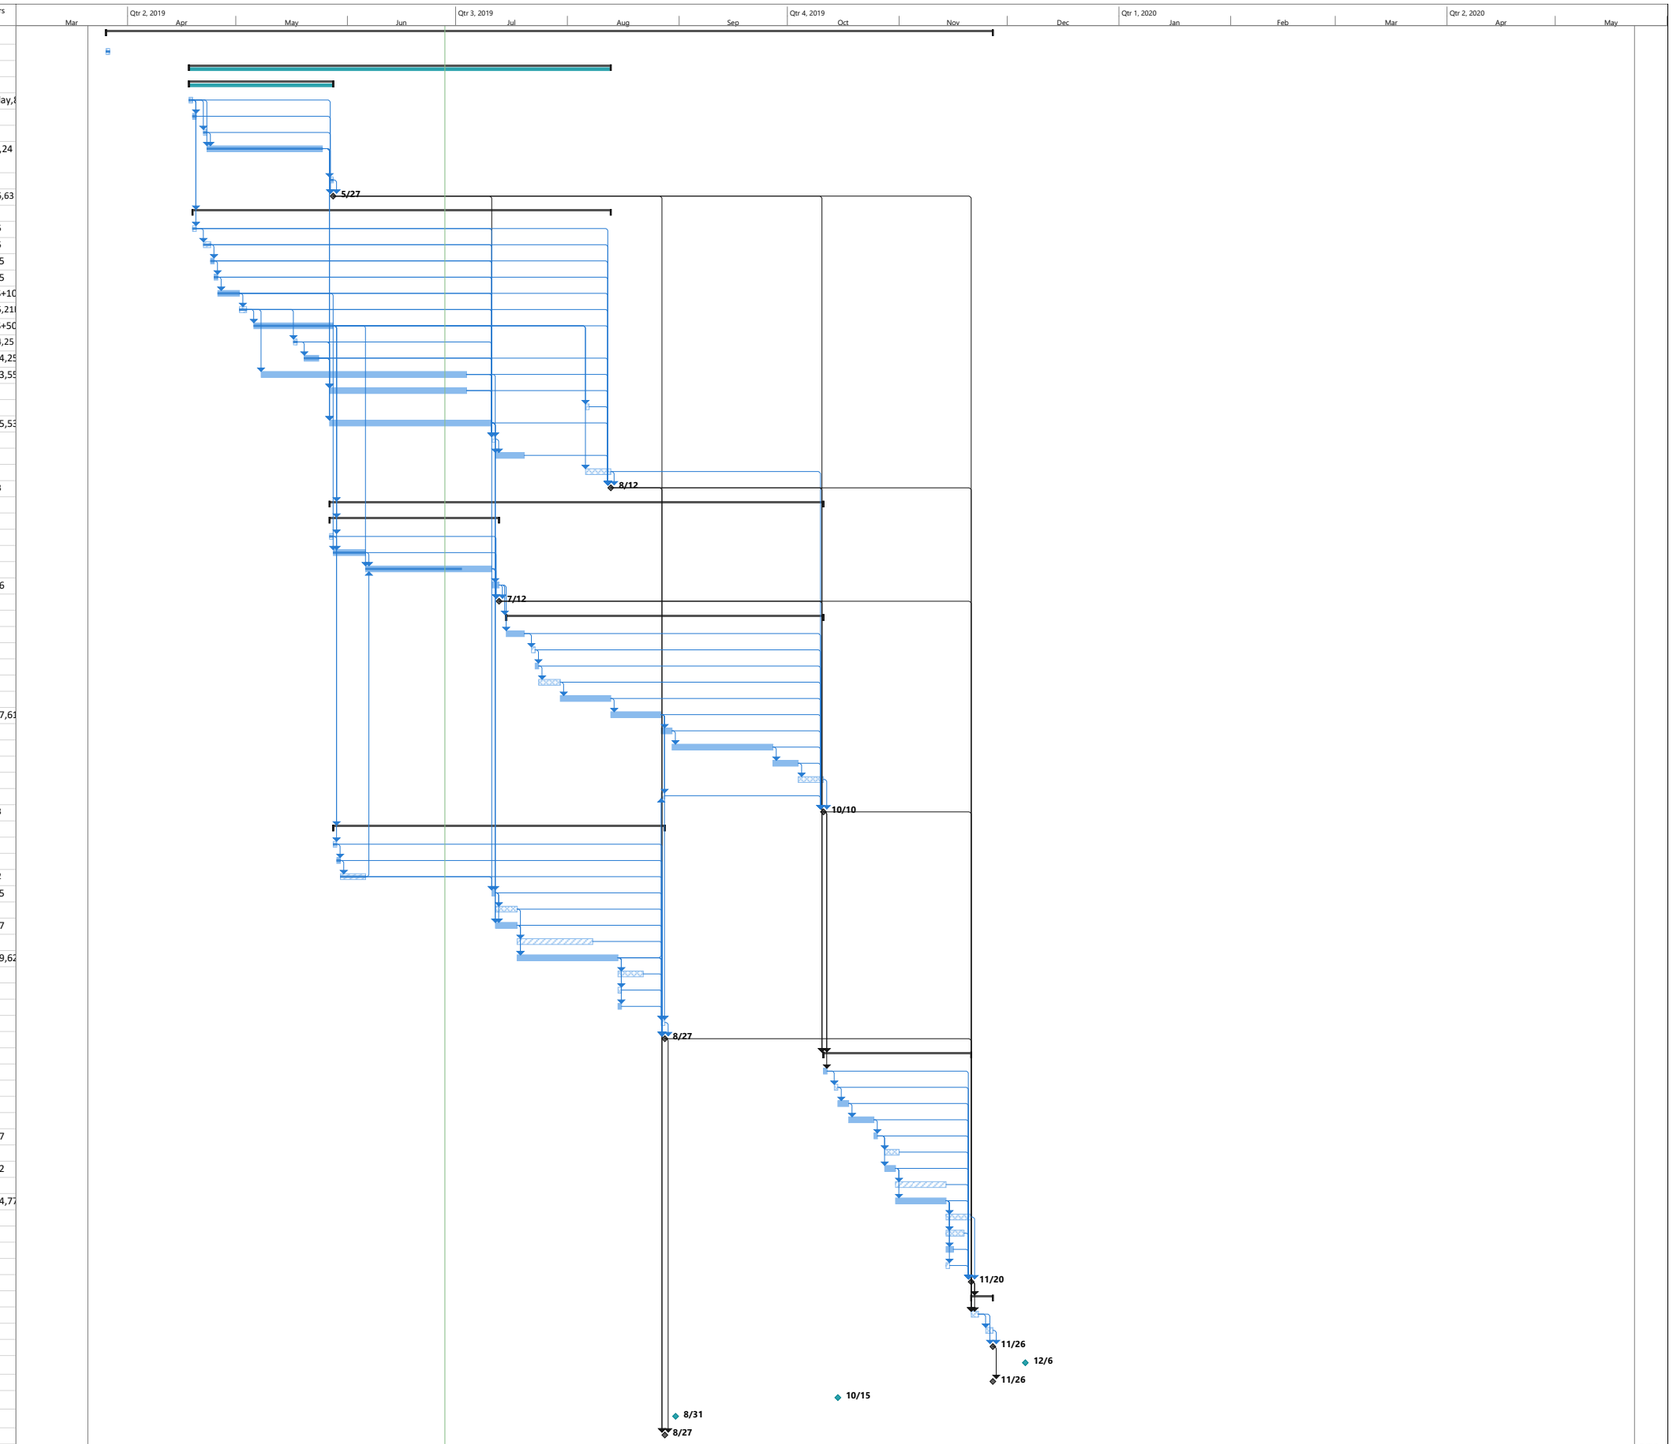

Project: Shelbyville East Washin
Date: Fri 6/28/19

Task | Split | Milestone | Summary | Project Summary | Inactive Task | Inactive Milestone | Inactive Summary | Manual Task | Duration-only | Manual Summary Rollup | Manual Summary | Start-only | Finish-only | External Tasks | External Milestone | Deadline | Progress | Manual Progress
